


Activity ID	Activity Name	Original Duration	Start	Finish	2009												2010												2011												2012																																																																																																											
					D	J	F	M	A	M	J	Jul	A	S	Oct	N	D	J	F	M	A	M	J	Jul	A	S	Oct	N	D	Jan	F	M	A	M	J	Jul	A	S	Oct	N	D	J	F	M																																																																																																								
SUNY Albany 500 Bed Facility					918.0d																																																02-Feb-09 A																																																27-Aug-12																																															
Pre-Design					61.0d																																																02-Feb-09 A																																																31-Dec-09																																															
01	Pre-Design	30.0d	09-Feb-09 A	24-Feb-09 A																																																																																																																																																
41	SEQRA	1.0d	02-Feb-09 A	31-Dec-09																																																																																																																																																
Procurement					391.0d																																																23-Mar-09 A																																																07-Sep-10																																															
RFP Design					141.0d																																																23-Mar-09 A																																																11-Sep-09																																															
Phase One					54.0d																																																23-Mar-09 A																																																08-May-09																																															
A1000	Request for DASNY Term Consultant Services	5.0d	23-Mar-09 A	30-Mar-09 A																																																																																																																																																
A1010	Consultant Develop Proposal	20.0d	30-Mar-09 A	24-Apr-09 A																																																																																																																																																
A1020	DASNY Complete Work Authorization	10.0d	27-Apr-09	08-May-09																																																																																																																																																
Phase Two					141.0d																																																30-Mar-09 A																																																11-Sep-09																																															
02	NYS Contract Reporter Ad	5.0d	30-Mar-09 A	21-Apr-09 A																																																																																																																																																
03	Receive EOI's	15.0d	21-Apr-09 A	21-Apr-09 A																																																																																																																																																
04	Committee Review	10.0d	24-Apr-09 A	05-May-09																																																																																																																																																
05	Short List Approval	10.0d	06-May-09	19-May-09																																																																																																																																																
07	Proposal Development & Submission	30.0d	20-May-09	01-Jul-09																																																																																																																																																
08	Proposal Review	10.0d	02-Jul-09	16-Jul-09																																																																																																																																																
09	Interviews	5.0d	17-Jul-09	23-Jul-09																																																																																																																																																
10	Contract Out	20.0d	24-Jul-09	20-Aug-09																																																																																																																																																
11	Contract Back	15.0d	21-Aug-09	11-Sep-09																																																																																																																																																
RFP Construction					238.0d																																																30-Sep-09																																																07-Sep-10																																															
Phase One					95.0d																																																30-Sep-09																																																15-Feb-10																																															
12	Contractor EOI	10.0d	30-Sep-09	13-Oct-09																																																																																																																																																
13	Committee Review	20.0d	14-Oct-09	10-Nov-09																																																																																																																																																
14	Bid Development & Prebid Meeting	30.0d	11-Nov-09	24-Dec-09																																																																																																																																																
15	Bid Opening	0.0d		24-Dec-09																																																																																																																																																
16	DASNY Issue LOI	35.0d	28-Dec-09	15-Feb-10																																																																																																																																																
Phase Two					95.0d																																																23-Apr-10																																																07-Sep-10																																															
17	Contractor EOI	10.0d	23-Apr-10	06-May-10																																																																																																																																																
18	Committee Review	20.0d	07-May-10	04-Jun-10																																																																																																																																																
19	Bid Development & Prebid Meeting	30.0d	07-Jun-10	19-Jul-10																																																																																																																																																
20	Bid Opening	0.0d		19-Jul-10																																																																																																																																																
21	DASNY Issue LOI	35.0d	20-Jul-10	07-Sep-10																																																																																																																																																
Design					273.0d																																																11-May-09																																																07-Jun-10																																															
Phase One					130.0d																																																11-May-09																																																11-Nov-09																																															
21a	Site Utilities - 30%	40.0d	11-May-09*	07-Jul-09																																																																																																																																																
22	Design Review - 30%	10.0d	08-Jul-09	21-Jul-09																																																																																																																																																
23	Site Utilities - 60%	30.0d	15-Jul-09	25-Aug-09																																																																																																																																																
43	Design Review - 60%	10.0d	26-Aug-09	09-Sep-09																																																																																																																																																

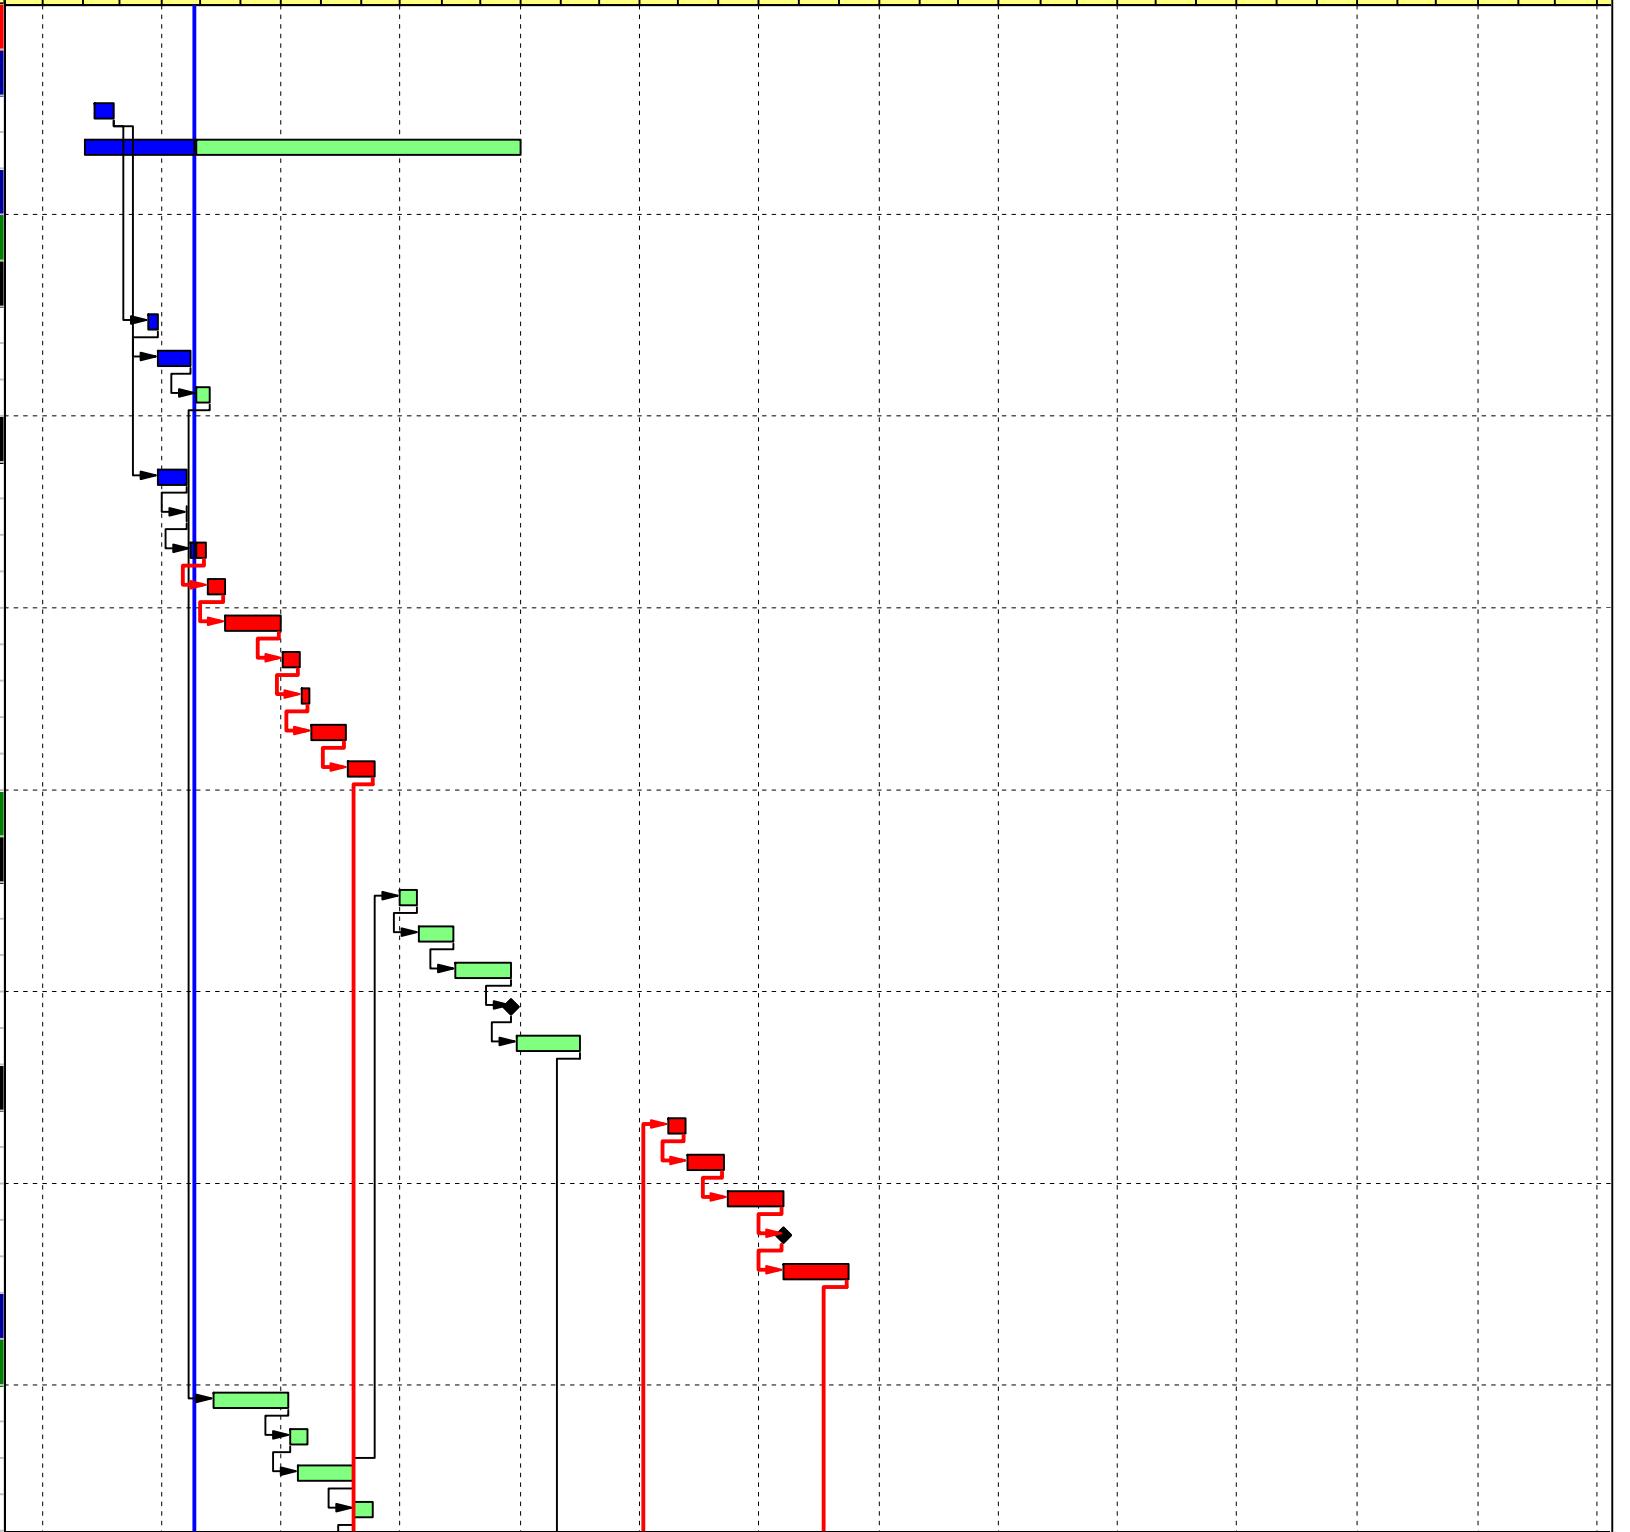

█ Remaining Level of Effort █ Non-Critical
█ Actual Level of Effort █ Critical Path
█ Actual Work ◆ Milestone

Preliminary Bid Schedule

Data Date: 27-Apr-09

For Discussion Purposes Only

Lt01 - All Activities

Page No. 1

