

DESIGN PROFESSIONAL'S GUIDE



January 2023

Corporate Headquarters
515 Broadway
Albany, NY 12207-2964
518-257-3000

New York City Office
28 Liberty Street, Fl 55
New York, NY 10005
212-273-5000

Buffalo Office
6047 Transit Rd., Suite 103
Buffalo, NY 14051
716-884-9780

Rochester Office
3495 Winton Place, Bldg. C, Suite 1
Rochester, NY 14623
585-450-8400

Table of Contents

ARTICLE 1 – DASNY	3
SECTION 1.1 - BACKGROUND	3
SECTION 1.2 - MISSION STATEMENT	3
SECTION 1.3 - CODE OF BUSINESS ETHICS	3
SECTION 1.4 - OPPORTUNITY PROGRAMS	3
SECTION 1.5 - LEADING IN ENERGY EFFICIENT SUSTAINABLE DESIGN AND CONSTRUCTION	3
SECTION 1.6 – GOVERNANCE	4
ARTICLE 2 – CONSTRUCTION DIVISION	5
SECTION 2.0 – The DASNY PM	5
SECTION 2.1 – PROCUREMENT	6
SECTION 2.2 – DESIGN REVIEW & TECHNICAL SUPPORT SERVICES	6
SECTION 2.3 – DESIGN AND CONSTRUCTION	7
SECTION 2.4 - CODE COMPLIANCE	7
SECTION 2.5 - PROJECT CONTROLS	7
ARTICLE 3 –PROJECT DELIVERY METHODS	8
SECTION 3.1 - PROJECT DELIVERY METHODS (Introduction)	8
Section 3.1.1 - Multiple Prime Contracts (Wick’s Law)	8
Section 3.1.2 - Other Project Delivery Methods	9
Section 3.1.3 - Job Order Contracting (JOC) Program	9
Section 3.1.4 - GC Minor Maintenance (GCMM) Program	9
ARTICLE 4 – PHASES OF A PROJECT	10
SECTION 4.1 - CONSULTANT SELECTION PHASE	10
Section 4.1.1 - Selection of the Design Professional	10
SECTION 4.2 – PRE-DESIGN PHASE	10
Section 4.2.1 – Submitting a Proposal for a Work Authorization	10
Section 4.2.2 - Scope, Budget and Schedule Confirmation	10
Section 4.2.3 - Project Budget	11
SECTION 4.3 - DESIGN PHASE	11
Section 4.3.1 - Design Quality	11
Section 4.3.2 - Design Professional Payments	11
Section 4.3.3 - Design Kickoff	12
Section 4.3.3.1 – Owner’s Project Requirements (OPR)	12
Section 4.3.5 - Sustainable Design	13
Section 4.3.6 – New York Legislation and Directives Related to Sustainable Design	15
Section 4.3.7 - Design Submission Requirements	15
Section 4.3.8 - Drawings	16
Section 4.3.9 - Project Manual	17
Section 4.3.10 - Technical Specifications	17
Section 4.3.11 - Submission Review Requirements	18
Section 4.3.12 - Cost Estimates	19
SECTION 4.4 - BID PHASE	19
Section 4.4.1 - Project Manual	19
Section 4.4.2 - Modifications to the General Requirements	21
Section 4.4.3 - Alternates	21
Section 4.4.4 - Allowances	22
Section 4.4.5 – Schedule of Allowances	22
Section 4.4.6 - Bid Documents	22
Section 4.4.7 - Pre-Bid Meeting	23
Section 4.4.8 - Addenda	23
Section 4.4.9 -Bids	23
Section 4.4.10 - Post Bid Requirements	23
SECTION 4.5 - CONSTRUCTION & CLOSEOUT	25
Section 4.5.1 - Construction Phase	25
Section 4.5.2 - Project Close-Out	25

ARTICLE 1 -- DASNY

SECTION 1.1 - BACKGROUND

The Dormitory Authority of the State of New York (DASNY) is a public benefit corporation; an independent corporate agency with governmental functions delegated to it by the State of New York and is authorized to finance, design, construct or rehabilitate buildings for the use by various public and private not-for-profit entities.

This Design Professional's Guide is intended to summarize, supplement and clarify various DASNY requirements. In the event of any conflict between this guide and the Contract, please consult with the DASNY PM for clarification and direction. The intended audience are the Design Professionals that DASNY contracts with to deliver projects. Additionally, this guide may be of use to other consultants, construction managers, clients and DASNY staff in their roles in delivering projects for DASNY.

SECTION 1.2 - MISSION STATEMENT

"We commit to **deliver exceptional service** and professional expertise on every **financing and construction project** for our **clients and the public**, in a **cost-effective** manner, while **advancing the policy goals of New York State.**"

SECTION 1.3 - CODE OF BUSINESS ETHICS

DASNY expects the highest degree of ethical business conduct by its employees and the many contractors, consultants and vendors with whom it interacts on behalf of its clients, bondholders and the people of the State of New York. DASNY administers a comprehensive corporate integrity program to ensure that DASNY, its officers and employees perform their official duties consistent with the requirements of the *New York State Public Officers Law*; other applicable laws, rules, and regulations; and policies of DASNY.

DASNY encourages and supports a fair, open and honest business relationship with its contractors, consultants and vendors based on quality, service and cost. Moreover, DASNY believes that a "level playing field" in the marketplace can only be achieved through adherence to ethical business practices by all participants involved in the process.

SECTION 1.4 - OPPORTUNITY PROGRAMS


Pursuant to provisions of the Request for Proposal, the Design Professional will be required to, in addition to any other nondiscrimination provision of the Contract and at no additional cost to DASNY, fully comply and cooperate with DASNY in the implementation of NYS Executive Law Article 15-A, participation by Minority Group Members and Women and NYS Executive Law Article 17-B, participation by Service-Disabled Veteran-Owned Businesses (SDVOBS) with respect to State Contracts. These requirements will include: equal employment opportunities for minority group members and women (EEO), plus opportunities for minority and women-owned business enterprises (M/WBE) and Service-Disabled Veteran-Owned Businesses. The Design Professional's demonstration of good faith efforts shall also be a part of these requirements.

SECTION 1.5 - LEADING IN ENERGY EFFICIENT SUSTAINABLE DESIGN AND CONSTRUCTION


DASNY is committed to promote the design and construction of energy efficient, sustainable public buildings, the sustainable use of resources, and in collaboration with other government agencies in pursuit of energy efficient policies, projects and technology that benefit New York State and New Yorkers. DASNY's commitment to sustainability is designed to produce a new generation of highly energy-efficient and environmentally responsible public-purpose buildings across the State.

SECTION 1.6 – GOVERNANCE

DASNY is governed by an eleven-member Board composed of the Director of the Budget, the Commissioner of Education of the State, the Commissioner of Health of the State, the State Comptroller or one member appointed by him or her, five members appointed by the Governor, with the advice and consent of the Senate, one member appointed by the Temporary President of the State Senate, and one member appointed by the Speaker of the State Assembly. DASNY's operating activities are managed through the Executive Staff and illustrated as follows:



DASNY's two primary lines of business are debt issuance and construction management, which are supported by DASNY's operating activities. As a part of its operating activities, DASNY devotes significant efforts to the administration of grants authorized by the State and payable to a variety of public and private grantees from proceeds of bonds issued by DASNY. DASNY has a staff located in four main offices (Albany, New York City, Rochester and Buffalo) and at field sites across the State. DASNY provides services to various clients under three major programs: Higher Education; Health Care and Government; and Non-Profit Agencies. The focus of this guide is DASNY's construction management activities, which are managed through the Construction Division and illustrated as follows:

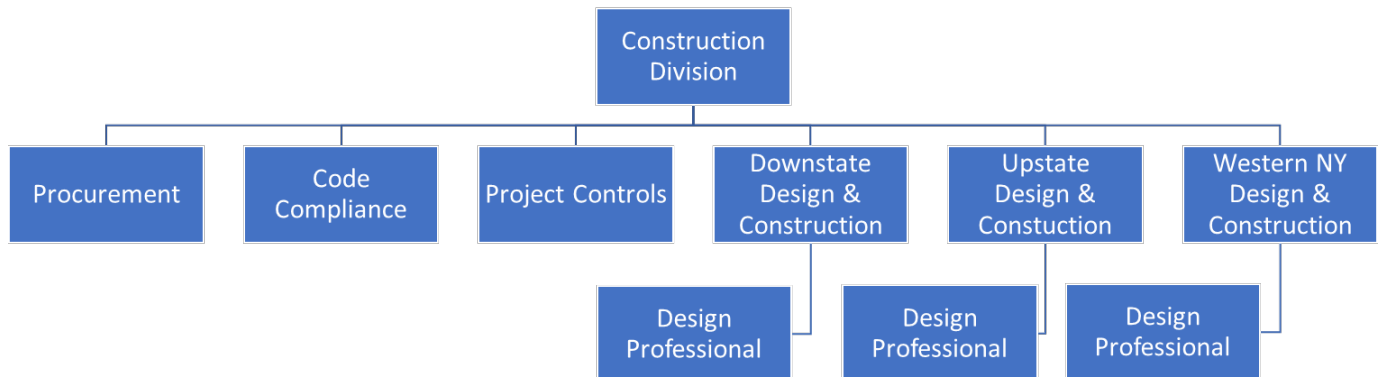


ARTICLE 2 -- CONSTRUCTION DIVISION

SECTION 2.0 – The DASNY PM

The **DASNY PM** is DASNY's primary point of contact for the Design Professional and the Client. Depending upon the project type, location, complexity, and phase, the **DASNY PM** may be a Design Phase Manager, Design PM, Construction PM or Project Manager. For simplicity's sake, this document will use the terminology "**DASNY PM**".

The **DASNY PM** is responsible for the execution of the contract, authorizing adjustments to the contract, and approving payments. All correspondence directed to DASNY relating to the project shall be addressed to the assigned **DASNY PM**.

The **DASNY PM** is the liaison between the Design Professional, the Client, and/or the Client Central Office. The Design Professional and all subconsultants are to report only to the assigned **DASNY PM**. See the functional relationship chart:

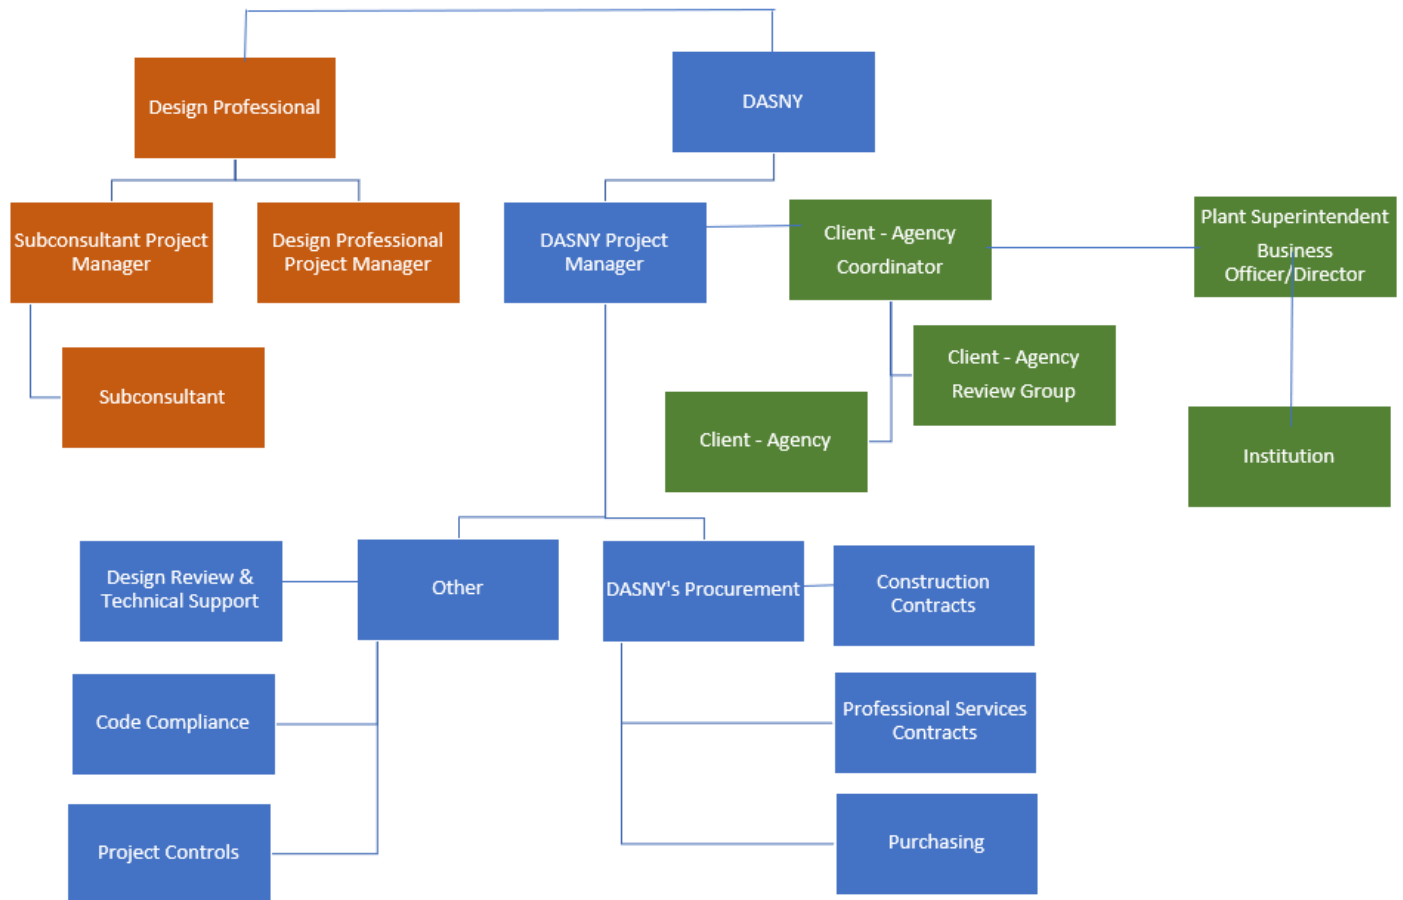

The DASNY PM is responsible to provide guidance to the Design Professional and to monitor its performance. It is the responsibility of the Design Professional to provide adequate supervision of its staff. Under no circumstances shall the DASNY PM directly supervise the staff of the Design Professional.

If a Design Professional or a subconsultant is contacted by the Client Central Office or the Facility, whether by written or verbal communication, they are to relay all information to the DASNY PM immediately. The Design Professional must phone the DASNY PM and e-mail a copy of the information. This action will keep the DASNY PM advised at all times so the DASNY PM can effectively manage the project and maintain the working liaison relationship throughout the project.

SECTION 2.1 – PROCUREMENT

Procurement develops all contracts issued by DASNY. The staff is organized into three groups: **(1) Professional Services Contracts** administers a centralized Request for Proposal process to procure professional services on specific projects and term contracts; **(2) Construction Contracts** manages the bid and construction contract award process, and administers the Job Order Contracting program that issues construction work orders and **(3) Purchasing** administers the procurement of furniture, fixtures and equipment, and coordinates the provision of in-house interior design services on selective projects.

Types of Contracts: Two types of professional services contracts are available: (1) Standard **Professional Services Contract** which is executed for a specific project and (2) **Professional Services Term Contract** which is executed for specific regions of the State, has term limits, is applicable to project values under \$25 million, and may also be issued for specific requirements as deemed necessary by DASNY. Each contract is comprised of three chapters, Chapter One–Project Terms and Conditions, Chapter Two–Professional's Required Services and Chapter Three–General Terms and Conditions. Contact DASNY for a sample.

Potential Contracting Opportunities: DASNY solicits for professional contracting opportunities in several ways. The two most common are as follows:

(2 Step Process): A selection committee is formed that includes project stakeholders, who establish qualification-based criteria sufficient to develop an approved short-list of the most qualified Design Professionals. A prospective professional services contract opportunity is advertised in the NYS Contract Reporter and posted on DASNY's web site: www.dasny.org. The Design Professional responds in writing, and meeting the specific advertisement requirements may place the Design Professional on the long-list of firms to be considered. Each Design Professional on the short-list may receive a Request for Proposal that defines the initial project scope, budget, schedule and proposal requirements, as well as delineates the selection process. Upon final selection of the Design Professional, a fee is negotiated and the standard Design Professional's Contract is executed. Compensation for Term Contracts is based on specific project or service needs and either a not-to-exceed negotiated fee is established or the Term Contract Consultant Fee Schedule included as part of the contract.

(1 Step Process): A selection committee is formed that includes project stakeholders, who establish qualification-based criteria sufficient to select and recommend the most qualified Design Professionals. A prospective professional services contract opportunity, inclusive of the Request for Proposal (RFP), is advertised in the NYS Contract Reporter and posted on DASNY's web site: www.dasny.org. The RFP defines the initial project scope, budget, schedule and proposal requirements, as well as delineates the selection process. The Design Professional responds in writing, and a committee, selected by DASNY, evaluate the proposals based upon criteria established by the committee. Proposals are evaluated to ensure that they meet the specific advertisement and Request for Proposal (RFP) requirements. The committee makes a recommendation to select and tentatively award contracts to the most qualified Design Professional(s). Upon final selection of the Design Professional(s), a fee is negotiated and the standard Design Professional's Contract is executed. Compensation for Term Contracts is based on specific project or service needs and either a not-to-exceed negotiated fee is established or the Term Contract Consultant Fee Schedule included as part of the contract.

SECTION 2.2 – DESIGN REVIEW & TECHNICAL SUPPORT SERVICES

DASNY's Construction Division staff manages the Design Professional and contract requirements from project inception through the Design, Procurement, Construction and Close-Out of the project. DASNY Construction Division staff is comprised of project managers, licensed architects and engineers and code enforcement officials, partnered with DASNY's client and design consultants. DASNY Construction Division staff monitors project scope, budget and schedule, coordinates in-house design reviews, issues review comments to the Design Professional. Although these functions help to ensure the contract documents comply with process, program, codes, rules and regulations, they are not intended to replace the Design Professional's quality functions. Some of DASNY's staff

Architects and Engineers are organized in the PDQA unit, providing support in planning, design and quality assurance (PDQA).

SECTION 2.3 – DESIGN AND CONSTRUCTION

Divided into Upstate (north of the Bronx), Downstate (NYC 5 boroughs & Long Island) and Western (West of Syracuse), Design and Construction manages the Design Professional and contract requirements from design phase through the bid, contract award, and construction/close-out phases of the project. In partnership with the Design Professional, staff from the Design and Construction group initiates design and the bid process and recommends award of contracts and provides construction management services through completion of the project. With the largest number of personnel within DASNY, experienced staff is strategically placed in DASNY's main offices and field office sites throughout the State for the benefit of the project.

SECTION 2.4 - CODE COMPLIANCE

Code Compliance administers and enforces the NYS building codes where DASNY participates in the construction of a building, or performs work on premises in the custody of a state agency and oversees the requirements identified in the NYS Statement of Special Inspections and Tests, which is prepared by the Design Professional and included within the contract documents. Code Compliance issues the Construction Permit and the Code Compliance Certificate (CCC) on NYS owned projects. For projects permitted by other Authorities Having Jurisdiction (e.g., NYC) in which DASNY participates, Code Compliance provides plan reviews with a focus on fire life safety systems and oversees the Special Inspection and Testing requirements. Code Compliance also provides environmental reviews, technical support, and compliance inspections for all DASNY projects.

Standard Specification Sections: Code Compliance maintains several standard technical environmental specification sections that are available to the Design Professional (obtained from the design phase manager) for edit to project specific requirements. These sections include but are not limited to: Asbestos Master Spec (Upstate); Asbestos Master Spec NYC; Asbestos Master Spec CUNY; CMM Asbestos Master Spec; DASNY Mold Remediation Specification; DASNY Standard Lead Abatement Specification; DASNY Standard Specification for Identification and Disposal of Hazardous Waste; DASNY Universal Waste Specification; Excavation, Transport and Disposal of Contaminated Soils; Lead Safe Work Practices (OSHA) for Disturbances of LBP/LCP; UST Removal Specification; Minor Asbestos Spec; and PCB Caulk Master Spec. DASNY also maintains the Standard Firestopping Specification.

SECTION 2.5 - PROJECT CONTROLS

Project Controls services include monitoring of project performance; ensuring deliverables are received from DASNY's construction consultant in a timely fashion, schedule review and cost estimating/cost control of projects. DASNY's Project Controls Group also reviews all change orders over \$5,000 and all construction claims. Project Controls also provides litigation support to DASNY's office of Counsel when and if necessary.

DASNY is utilizing enhanced technology including PMWeb and Contract Management™ project management software applications and added an enterprise scheduling system (Primavera P6) to provide accurate schedule reporting across all programs. These construction applications, utilized by DASNY and the Design Professional, provide timely and accurate information so all are kept informed of issues that impact the project. If needed, DASNY can provide to the Design Professional training in the use of PMWeb. PMWeb shall be utilized by the Design Professional as the primary project management and document controls systems from project inception through design and construction completion, unless otherwise directed by DASNY.

Project Controls also provides construction management orientations with the goal of introducing construction consultants to DASNY's process of conducting business and project health assessments ("PHAs") for capital projects to ensure that construction consultants are delivering services in accordance with DASNY expectations.

ARTICLE 3 –PROJECT DELIVERY METHODS

SECTION 3.1 - PROJECT DELIVERY METHODS

Introduction

As a public authority, DASNY has a number of project delivery methods available for its use. The actual method used by DASNY is dependent upon the client for whom the work is being performed, the legislative authority governing DASNY's relationship with the client and the project requirements. The Design Professional will be informed of the delivery method being employed either as part of the selection process or as information from the DASNY PM, early in the Project's design phase. See below for a brief overview of some of the more common project delivery methods.

Section 3.1.1 - Multiple Prime Contracts (Wick's Law)

General Municipal Law and State Finance Law requires DASNY to prepare specifications to permit separate and independent bidding for three subdivisions of work for some of its clients when the entire cost of construction or alteration exceeds the following thresholds, or as revised by subsequent legislation:

New York City - \$3 million

Long Island and Westchester - \$1.5 million

Upstate - \$500,000

These requirements (Wick's Law) apply to many DASNY programs, including its public clients and some private clients. Most private clients and projects performed by DASNY for the State University of New York generally are not bound by the requirements, although locally sponsored community colleges are subject to Wick's Law. The Design Professional shall review the requirements for multiple prime contracts with the DASNY PM. NOTE: DASNY currently has [Project Labor Agreements \(PLAs\)](#) in place for projects within the five boroughs of NYC for projects greater than \$3 million in construction value. These projects are not governed by Wicks Law and are therefore single prime. Even if a project is a single prime contract, generally the prime contractor is required to name their HVAC, Plumbing and Electrical subcontractors at the time of bid, so the Contract Documents must include a basis upon which the scopes of these subcontracts can be equitably based and compared.

When a project is subject to the Wick's Law, the Design Professional must prepare separate but coordinated Bid Documents using the General Requirements for Multiple Prime Contracts.

The three required trades are:

- heating, ventilating and air conditioning (HVAC)
- plumbing
- electrical

A construction contract may also be required. On public work projects subject to Wick's Law, the construction contractor cannot be assigned responsibility for coordination of the separate prime contracts. Coordination among the prime contracts is the responsibility of DASNY, who may delegate it to the Design Professional or construction manager.

DASNY may require the Design Professional to prepare Bid Documents for more than four prime contractors, depending on the size, scope and complexity of the project.

Section 3.1.2 - Other Project Delivery Methods

In addition to a design-bid-build multiple prime Wick's Law project, DASNY may undertake a project using other project delivery methods that may affect the Design Professional's scope of services. Such methods may include: Construction Manager at-Risk, CM-Build, Single Prime Contracting, Design-Build, Energy Performance Contracting (EPC), Job Order Contracting (JOC) and GC Minor Maintenance.

Project Labor Agreement (PLA): The PLA is a collective bargaining agreement for particular construction projects or group of construction projects that establishes uniform terms and conditions for labor. On certain projects within the five boroughs of New York City (NYC), DASNY may perform a study in order to substantiate projected cost savings and, if so, initiate a PLA. Projects administered under a PLA exempt it from Wick's Law requirements. Details of the DASNY PLA agreement may be found on DASNY's web site: www.dasny.org.)

Section 3.1.3 - Job Order Contracting (JOC) Program

Under its Job Order Contracting (JOC) Program, DASNY has awarded competitively bid contracts to general construction, HVAC, plumbing, electrical, asbestos abatement and other contractors to provide construction services throughout the state at pre-determined unit prices. When appropriate, JOC work is identified and approved, DASNY then issues a contract ("job order") for a lump sum amount based on pre-determined unit prices multiplied by quantity and by the JOC contractor's adjustment factor. The Procurement Department administers the JOC Program with the assistance of its consultant.

Except in the case of emergencies, the design for a JOC project must be reviewed and approved by DASNY before DASNY will authorize the contractor to begin work. The number of design submissions will be commensurate with the scope of the project. As little as one submission may be required, or a full set of 30%, 60%, and 100% documents may be required. Contact the DASNY PM to determine the appropriate requirements. The documents required for review will differ for each job order and can range from a single stamped drawing to a complete set of drawings and specifications. The DASNY PM will determine the documents required for each JOC project.

Section 3.1.4 - GC Minor Maintenance (GCMM) Program

The GC Minor Maintenance delivery method is for projects with a construction value of less than \$80,000. General Contractors are under contract regionally. The contract award is based upon a mark-up percentage applied to the cost of sub-contracted work. Currently, this method can be used for OMH, OPWDD, OASAS and SUNY.

ARTICLE 4 – PHASES OF A PROJECT

SECTION 4.1 - CONSULTANT SELECTION PHASE

Section 4.1.1 - Selection of the Design Professional

A project starts with a request from one of DASNY's clients. The project is assigned to a DASNY PM.

For projects with a construction value of less than \$25.0 million, DASNY may select a Design Professional from an approved list of term Design Professionals who were awarded contracts via the advertisement/RFP process. The DASNY PM follows internal procedures for assigning a specific project to a Term Design Professional. Project fees are determined on either a fee schedule basis ([DASNY Term Contract Consultant Fee Schedule](#)) or on a negotiated basis. Term Design Professionals' contracts, assignments, performance and workload are reviewed periodically, and new Term Design Professional solicitations are initiated in the NYS Contract Reporter as appropriate.

For projects with a construction value of greater than \$25.0 million or greater, a selection committee is formed by the procurement team that typically includes key DASNY personnel, client representatives and project stakeholders, who establish qualification-based criteria sufficient to develop an approved short-list of the most qualified Design Professionals. The Design Professional responds in writing, and, meeting the specific advertisement requirements, may place the Design Professional on the long-list of firms to be considered. Each Design Professional on the short-list may receive a Request for Proposal that defines the initial project scope, budget, schedule and proposal requirements, as well as delineates the selection process. Upon final selection of the Design Professional, a fee is negotiated and the standard Design Professional's Contract is negotiated and a contract is executed. The selection of Design Professionals is a Qualifications Based Selection (QBS).

The Design Professional must continue to provide DASNY with proof of valid insurance throughout the life of the contract. Failure to do so may be grounds for termination.

SECTION 4.2 – PRE-DESIGN PHASE

Section 4.2.1 – Submitting a Proposal for a Work Authorization

The Design Professional shall submit a proposal where the Design Professional will perform the work for the values outlined in DASNY's Fee Schedule, shall include their Scope of Services, correspondence indicating their acceptance of the Fee Schedule and an executed [Scope, Budget and Schedule Confirmation form](#). Where projects warrant a fee different from DASNY's Fee Schedule, the proposal shall include all of the items outlined above, except the correspondence regarding the Fee Schedule, but include the consultant-specific "Term E-Forms," for each consultant and sub-consultant that will be utilized to complete the scope of services.

Section 4.2.2 - Scope, Budget and Schedule Confirmation

The success of any project is having a complete scope of work and a sufficient budget. The client develops a preliminary project scope and budget, with or without professional assistance. The scope, budget and schedule confirmation process is used to confirm that the requested scope of work is adequate to satisfy the objective of the project, including established sustainability goals, and that the approved funds are sufficient to support this initiative. Confirmation of the scope and budget is also a requirement of many of the Project Management Agreements (PMA) between DASNY and its clients and is a requirement of the contract between DASNY and the Design Professional. The executed [Scope, Budget and Schedule Confirmation Form](#) will also serve to determine the schedule for the project and provide a Design start date, a bid date and a construction completion date, and any other milestone dates required for the completion of the project. As a means of further developing the scope, budget and schedule, DASNY may elect to authorize the Design Professional to proceed only through

the initial phases of design prior to contracting for the full scope of services. If this approach will be used, the DASNY PM will inform the Design Professional of the design phase they shall work through, early in the Project's design phase.

Section 4.2.3 - Project Budget

The Project Budget is established based on the intended project scope and the available or forecasted funding of the project. Key to the success of a DASNY project is managing the design within the "Approved Construction Budget" as established by the DASNY PM. It is the responsibility of the Design Professional to manage the project design within the "Approved Construction Budget" for the Design Professional's scope of services.

The "Approved Construction Budget" as used in the Scope, Budget and Schedule Confirmation form, refers to the amount of the project budget that will be expended in constructing the project and for which the design professional is providing services. The "Approved Construction Budget" does not include design fees, land acquisition, or other project costs for which the Design Professional is not providing services. Furniture, fixture and equipment (FF&E) costs, change order, and contingency costs may be included in the "Approved Construction Budget", as appropriate, as determined by the DASNY PM.

SECTION 4.3 - DESIGN PHASE

Section 4.3.1 - Design Quality

The quality of the documents developed by the Design Professional is of paramount importance to DASNY and its clients. The Contract Documents establish the contractual obligations between DASNY and the Contractors. The Contract Documents must have all trade disciplines coordinated, and must be sufficiently detailed to ensure competitive bidding, installation compatibility, and systems operation commensurate with the requirements of the project scope in accordance with the project schedule and within the project budget.

Regardless of any periodic or final review DASNY or its clients may make of the design, the Design Professional must take professional responsibility for the correctness and completeness of the Contract Documents and for conformance with applicable zoning requirements, codes, and laws. This includes coordination between the Design Professional and sub-consultants, which is the contractual responsibility of the Design Professional.

The periodic reviews conducted by the PDQA staff do not take the place of the Design Professional's quality control and quality assurance programs. The Design Professional shall be responsible for a fully coordinated, technically correct, and code compliant set of documents. The Design Professional may be required to have a formal, written quality program. DASNY, at its discretion, may require the Design Professional to provide a copy of this program for DASNY's review.

Section 4.3.2 - Design Professional Payments

The Design Professional may submit for payment after contract execution and the provision of acceptable deliverables. For projects managed in PMWeb, this is done electronically. For projects in Contract Management, payment requisitions must be made on the Application for Payment form as provided by the DASNY PM, depending on the phase of the project. Appropriate supporting documentation, such as timecards, receipts for reimbursable items, and other requested documentation must be attached. Submit two copies with original signatures to the DASNY PM. Payment requisitions should be submitted monthly or as project milestones are completed, but in all cases project billings should be current. For additional information, review the [DASNY Payment Procedure Outline](#).

Design Professionals are normally paid once per month on one of two payment dates based a pre-established

payment cycle. The check dates are normally mid-month and end of month. Checks are typically issued within 30 calendar days of a properly submitted Application for Payment. ACH transactions are also available.

The Design Professional may submit a final application for payment upon completion of all its services. This normally will be at the point that final applications for payment have been submitted by the contractors and no further services are required of the Design Professional (except possibly warranty inspections).

Section 4.3.3 - Design Kickoff

The design phase begins with a design kickoff or orientation meeting. This will be scheduled by the DASNY PM at or about the time that the contract with the Design Professional is executed and approved, depending upon the project. Attendees at the design kickoff meeting generally include all participants with an interest in the project, including, but not limited to the Client, DASNY, key members of the design team, energy modeler, commissioning agent, and cost estimator. The agenda generally includes introduction of personnel involved in the project, discussion of administrative procedures, discussion of the **Owner's Project Requirements (OPR's)**, discussion of project scope, budget and schedule, hazardous materials and a site visit and walk-through. Contact the DASNY PM regarding additional agenda items. The Design Professional will be required to record attendance and prepare and distribute an agenda and minutes of the design kickoff meeting. The Design Professional will also be required to prepare a project directory of all participants, including name, title, address, phone and e-mail addresses.

Section 4.3.3.1 – Owner's Project Requirements (OPR)

The Owner's Project Requirements (OPR) is a document which provides information related to the Owner's goals and objectives for present needs and anticipated future conditions, collected and documented by DASNY and DASNY's Design Professional, resulting from discussion with DASNY's customer-agency at the inception of the project, prior to design efforts commencing.

The OPR is written documentation that details the functional requirements of the Project and the expected use and operation of the Project, including but not limited to the criteria for a successful Project, the Owner and Client requirements, the applicable regulatory and legal requirements, the environmental and sustainability goals, the energy efficiency goals, the indoor environmental quality requirements, the equipment and system expectations, the building occupant and operating and maintenance personnel requirements, measurable performance criteria, cost considerations, and other benchmarks and goals important to the Owner or Client. The OPR shall include the sustainability and energy performance goals for the project as may be required by the Project's Client's requirements, regulatory agencies and applicable laws and regulations.

The Design Professional shall confirm and develop the Owner's project goals and requirements with the project team, including the Owner, Client, and other stakeholders deemed necessary for determination of the goals for the project.

Section 4.3.4 - Code Requirements

In accordance with Part 1204 of Title 19 of the Official Compilation of Codes, Rules and Regulations of the State of New York, DASNY is designated as a Construction Permitting Agency and is responsible for the administration and enforcement of the New York State Uniform Fire Prevention and Building Code (Uniform Code) with respect to certain construction activities it undertakes. The Code Compliance Department is responsible for administration of the Construction Permitting Program. Projects in the following New York State programs (State operated facilities) are subject to the Construction Permitting Program:

- Department of Health (DOH)
- Office of Alcohol and Substance Abuse Services (OASAS) (state operated facilities only)
- Office of Mental Health (OMH)

- Office of People with Developmental Disabilities (OPWDD)
- State Education Department (SED)
- State University of New York (SUNY)

There may be extenuating circumstances requiring certain other projects be included in the Construction Permitting Program. In such cases, determination will be coordinated with the Code Compliance Department. When DASNY is the Code Permitting Agency, the design review process is integrated with the Construction Permitting process. Code Compliance maintains [Code Compliance Review](#) and [Statement of Special Inspections Forms](#) that shall be completed by the Design Professional and provided for review with each submission. All outstanding design review comments must be resolved to the satisfaction of PDQA and Code Compliance prior to issuing a Construction Permit. The Design Professional shall prepare and submit the DASNY Construction Permit Application provided by the DASNY PM.

Where DASNY participates in the construction of a new building or in the conversion, alteration, addition, or repair of an existing building and where upon its completion such building will be in the custody of an entity other than a state agency, post-CCC administration and enforcement of the Uniform Code or other applicable code will be the responsibility of the code enforcement agency generally performing those functions at the location of the work.

The New York City Department of Buildings (NYC DOB) governs permitting, construction and use of buildings within the five boroughs of New York City, with the exception of State owned and operated facilities. NYC DOB enforces the standards for construction, alteration, repair, demolition, removal, and maintenance of buildings and for the energy utilization/reduction, green-house gas reduction and sustainability performance of projects under its jurisdiction. Projects for which NYC is the authority having jurisdiction will be subject to review and approval by the appropriate regulatory agencies including by not limited to NYCDOB, FDNY, NYCDEP, NYCDOT, NYCLPC, etc. Projects in the following programs are subject to NYC DOB construction permitting and code enforcement:

- City University of New York (CUNY)
- Health and Hospitals Corporation (HHC)
- NYC Office of the Chief Medical Examiner (OCME)
- Office of Alcohol and Substance Abuse Services (OASAS), non-state operated facilities only
- NYC Court Facilities

Section 4.3.5 - Sustainable Design

DASNY is committed to being a leader in promoting sustainable design in the projects it designs, constructs, and manages for its clients. Many of DASNY's clients are mandated by New York State law or Executive Order to provide elements of sustainable design in their projects. Projects for which NYC is the authority having jurisdiction are subject to NYC code and regulatory requirements regarding the project's energy utilization/reduction, green-house gas reduction and sustainability performance. Sustainable design features do not always increase the project first cost and, when they do, these features generally provide a payback after construction due to decreased energy consumption or maintenance and operating costs.

DASNY encourages its clients and Design Professionals to implement innovative design solutions into every project in order to ensure the delivery of the most energy efficient and sustainable design possible. Specific strategies that have been successfully implemented on previous projects include:

- Highly energy-efficient heating and cooling systems.
- Building management systems to provide increased controllability of building systems.
- High performance glazing systems that minimize heat gain/loss and result in reductions in the sizing of HVAC systems.
- Day lighting principles to maximize light for occupants while minimizing energy consumption for artificial lighting.
- Highly-Efficient Building Envelopes
- Energy-efficient fixtures, devices, appliances, and equipment.
- Light-colored roofing systems to minimize heat gain during the cooling season.
- Indigenous vegetation to minimize water use and provide building shading during the cooling season.
- Locally produced materials.
- Recycled materials.
- Locating projects proximate to mass transit to minimize parking and vehicle use by occupants.

All projects must comply with the laws and executive actions that govern energy efficiency and sustainability within New York State. The Design Professional shall submit all obligatory documentation as required by the [Design Professional's Submission Requirements](#).

At a minimum, the Design Professional shall incorporate energy-efficient criteria consistent with the Energy Conservation Construction Code of New York State and any other energy efficiency levels as may be designated by the New York State Energy Research and Development Authority (NYSERDA) into all specifications developed for new construction and renovation. The Design Professional shall investigate the use of the services of a Technical Assistance Provider approved by NYSEDA, and discuss this engagement and any resulting recommendations with the DASNY PM. The Technical Assistance Provider can assist the Design Professional in analyzing the design and providing recommendations to maximize energy efficiency and to promote the eligibility of the capital cost incentives included in NYSEDA's New Construction Program. For further information refer to [NYSEDA's website](#).

The Design Professional shall investigate and ascertain available credits, incentives, and grants available from NYSEDA, DOE, EPA, NYS DEC and other state and federal agencies. These credits, incentives, grants shall be detailed in the schematic report, with the potential dollar value savings associated with each identified, along with capital costs and simple payback associated with each.

Commissioning is required on all DASNY projects unless otherwise noted. The Design Professional shall provide services as specified in the Contract scope of services and shall be in accordance with the latest version of DASNY's [Building Commissioning Guidelines](#).

Section 4.3.6 – New York Legislation and Directives Related to Sustainable Design

The Design Professional shall comply with the following legislation and directives regarding sustainable design, including, but not limited to:

New York State:

- Executive Order #22 – Leading by Example: Directing State Agencies to Adopt a Sustainability and Decarbonization Program
- Green Building Construction Act
- Climate Leadership & Community Protection Act

SUNY:

- Directive 1B-2 – Net Zero Carbon for New Buildings and Deep Energy Retrofits for Existing Buildings
- Directive 1B-7 – Sustainability & LEED Policies

New York City:

- NYC Energy Conservation Code (ECC)
- Local Law #92 – A Local Law to amend the New York City building code, in relation to requiring that the roofs of certain buildings be partially covered in green roof or solar photovoltaic electricity generating systems
- Local Law #94 – A Local Law to amend the administrative code of the City of New York and the New York City building code, in relation to requiring that the roofs of certain buildings be covered in green roofs or solar photovoltaic electricity generating systems
- Local Law #97 – A Local Law to amend the New York City charter and the administrative code of the City of New York, in relation to the commitment to achieve certain reductions in greenhouse gas emissions by 2050

Section 4.3.7 - Design Submission Requirements

The minimum requirements for design submissions shall be as described in the [Design Professional's Submission Requirements](#) and the Professional Services Agreement. The Design Professional shall review the Design Professional's Submission Requirements for each project and comply with those requirements as appropriate for the project scope. The Design Professional shall advise the DASNY PM of any requirements that they believe are not applicable to a specific project prior to preparation of the initial submission. DASNY shall make the final determination as to how the Design Submittal Requirements are applied to a specific project.

Design submissions include the Narrative, Drawings, Specification, a Project Manual, and other technical, Code, Zoning, Cost Worksheet, Sustainability, Meeting Minutes and Administrative information. If a design phase schedule with fewer submissions than the standard 30%, 60% and 100% (Schematic Design, Design Development and Construction Documents), has been agreed to by the DASNY PM, each submission must contain all the necessary information for that phase plus all the information required for the earlier phases that were not included in the schedule, so that the reviewers and others can understand the basis for the decisions. If the required information is not submitted, a resubmission of the phase will be required, causing unnecessary delays.

Projects lacking definitive scopes of work, requiring assessments, large or complex projects and new buildings may include studies, feasibility or investigation reports, preliminary pre-schematic or programming phases, or additional design phases and/or submissions. These will be defined by DASNY on a project-specific basis. The DASNY PM may also decide to hold periodic progress meetings and on-board reviews to expedite the process.

If a feasibility or pre-schematic phase was not conducted or if the information is not fully developed, the consultant shall fully investigate the existing conditions, program, regulatory requirements and site constraints at the inception of the 30% or Schematic Design Phase, in consultation with the Client Agency and DASNY.

During the 30% phase, the consultant shall develop several independent design schemes (typically 3, or as many as may be reasonably required by DASNY) to fully explore the range of reasonable options. The alternatives should be developed to a similar level and presented in scale and in context, in sufficient detail so that reasonable judgments of the advantages and disadvantages of each approach can be made. Each alternative shall be accompanied by a cost estimate, tabulation of programs spaces and/or other technical data, as applicable. The schemes and data shall be presented in comparison to the program requirements and project goals.

Generally, a meeting or series of meetings will be held for the consultant to present the design options to the Client Agency and DASNY. The consultant will lead a discussion among the project team members

Electronic copies of the DASNY logo and standard Project Manual cover sheet, drawing title sheet, and title blocks are available on the DASNY website under [Design & Construction Resources](#) or from the DASNY PM upon request. The Procurement Department will also provide a sample Project Manual cover sheet when the DASNY PM requests boilerplate documents for the project at the 60% submission phase or earlier depending on the scope of the project.

Section 4.3.8 - Drawings

Refer to the [Design Professional's Submission Requirements](#) for comprehensive requirements.

The Design Professional should provide the DASNY PM with a copy of the proposed title block prior to drawing production. The drawing title block must include DASNY's name, address, and logo, Design Professional name and address, client name, project location, project title, project number, sheet name, sheet date, sheet number, drawing scale, graphic scale, revision block, and block for seal and signature.

Drawings are to be prepared in CAD and/or BIM format approved by DASNY for the project, using layer conventions generally accepted in the industry, such as those published by the American Institute of Architects or the National CAD Standard.

Phase and interim submissions shall be in PDF format, 100% submissions shall be in PDF and record CAD/BIM formats as requested and approved by DASNY, or any other submission formats as may be required by DASNY.

The 100% submission and the subsequent bid document submission shall be signed and sealed by the Design Professional.

At the onset of a project, a decision will be made that determines if the project will be designed according to DASNY's [Building Information Modeling \(BIM\) Manual](#).

Section 4.3.9 - Project Manual

The Project Manual evolves from the design documents submitted at various stages to DASNY for review into the complete collection of documents on which contractors bid and which are subsequently incorporated into the Contract.

Each design submission should include a [Project Manual cover sheet](#).

Section 4.3.10 - Technical Specifications

Refer to the [Design Professional's Submission Requirements](#) for comprehensive requirements.

The technical specifications shall be included in the Project Manual and should in no case be written only on the drawings unless previous permission is granted by the DASNY PM. The specifications must be typewritten and utilize Construction Specifications Institute 3-part Master Format, the current edition.

The latest version of DASNY's Front-End Documents can be accessed from within DASNY's project management systems as follows:

- In Contract Management, they are attached to the project named 'FEDOCS – DASNY Front-End Documents'. To view the attachment, right-click on the FEDOCS project, and then select 'Project Settings' from the menu to open the 'Project Settings' pop-up window. Arrow over to the 'Attachments' tab to view the file.
- In PMWeb, they are attached in the Document Manager. To view the attachment, click on 'Tools' on the Control Panel and then choose 'Document Manager'. Scroll down to the folder named 'Shared Folders' and open the sub-folder named 'DASNY Forms for Consultants' to view the file.

The DASNY Front-End Documents are contained in a Zip file. Download the file named "CM Front End Documents" and then extract its contents. This creates two folders named Division 0 and Division 1. The folder Division 0 contains the Bidding Requirements, Contract Forms, and the General Conditions as PDF files. The folder Division 1 contains the General Requirements as editable Microsoft Word documents.

The make and model number of the product or system upon which a specification is based should be cited. At least three (3) manufacturers of equivalent products shall also be listed, to facilitate compliance with public bidding laws. The Design Professional must specify the features or attributes of the specified product or system that will be used to evaluate equivalents proposed by a bidder. The specification of proprietary products must be pre-approved by DASNY's President; the Design Professional should contact the DASNY PM for instructions. Sole or single sourced items, equipment and/or vendors shall be identified in the procurement checklist(s) and submitted as early as possible for a procurement exemption.

The Design Professional should consult with the DASNY PM if the use of performance-based specifications is being considered.

If the Design Professional is considering design delegation, refer to your Professional Services Agreement and contact your DASNY PM to discuss the approach. Design delegation shall be precluded to the extent possible and practicable, and if so considered for inclusion, must be identified and submitted to DASNY for approval prior to commencement of work.

Foreign sourced materials shall be precluded to the extent possible and practicable, and if considered for inclusion, shall be identified as early as possible and submitted to DASNY for approval. If the Design Professional is considering foreign sourced materials, refer to your Professional Services Agreement and contact your DASNY PM to discuss the approach.

If a project involves hazardous material remediation or asbestos abatement, the Design Professional shall use DASNY's standard specifications (refer to <https://www.dasny.org/DesignConstruction/Resources>) edited to reflect the project specific conditions and requirements:

- [DASNY Standard Asbestos Removal Specification \(Upstate\)](#)
- [DASNY Standard Asbestos Removal Specification \(NYC\)](#)
- [DASNY Standard Asbestos Removal Specification \(CMM Projects only\)](#)
- [DASNY Standard Asbestos Removal Specification \(CUNY\)](#)
- [DASNY Standard Asbestos Removal Specification \(Minor projects only\)](#)
- [DASNY Standard Specification for Identification and Disposal of Hazardous Waste](#)
- [Lead Safe Work Practices \(OSHA\) for Disturbances of LBP/LCP](#)
- [DASNY Standard Mold Remediation Specification](#)
- [Non-Liquid PCB Material Removal \(PCB Caulk\)](#)
- [Removal and Disposal of Universal Wastes Specification](#)
- [DASNY Standard Firestopping Specification](#)
- [DASNY Standard Lead Abatement Specification](#)
- [Underground Storage Tank \(UST\) Removal Specification](#)
- [Excavation, Transport and Disposal of Contaminated Soils](#)

The technical specifications shall also include the [DASNY Standard Roofing Warranty](#) on projects involving roof replacement and installation.

Section 4.3.11 - Submission Review Requirements

In an effort to ensure that DASNY projects are code compliant, are technically sound, and that Contract Documents are clear and understandable, DASNY reviews all design submissions. This process is designed to protect bondholders, minimize errors and omissions, and comply with statutory requirements.

The DASNY PM will establish the process for the review of submissions and the timeframe required/allowed.

Design submissions generally consist of Schematic Design (30%), Design Development (60%), and Construction Documents (100%). The number and levels of submissions shall be as defined by the contract between DASNY and the Design Professional. On smaller projects, projects with a well-defined scope, or as may be required and approved by DASNY, the standard phase submissions may be combined or eliminated. Pre-schematic submissions and additional interim submissions may be required when warranted by the project scope and as directed by the DASNY PM. Contact the DASNY PM for clarification and to determine the number of copies and distribution required for each submission. Design submissions shall include construction cost estimates, design, procurement and construction schedules, regulatory approval submission plans and filing schedules, and DASNY procurement checklist(s).

Typically, the 100% submission consists of an initial or 90% submission for review which shall be unsigned and unsealed, and a subsequent 100% signed and sealed set of construction documents for final review prior to bid. Depending upon the nature and extent of DASNY's comments on the 90% or 100% design submission, a design re-submission may be required and an additional full review cycle conducted before the project may proceed to the Bid Documents Phase. Alternatively, if the 100% design submission comments are minimal or minor, the project may proceed to the Bid Documents Phase without a re-submission if approved by DASNY.

DASNY's Design and Construction unit and Code Compliance units will provide written comments for each

design submission. These comments are currently electronically prepared using [ProjNet DrChecksSM](#) and shall be provided via the approved current system or other system(s) as accepted by DASNY. The Design Professional is required to prepare responses to the comments provided in DrChecksSM (or other system(s) as accepted by DASNY). Submissions received without responses to previously provided design review comments will be returned to the Design Professional until responses have been provided.

The Design Professional is encouraged to discuss all questions and comments from design reviews directly with DASNY's Design & Construction and Code Compliance staff. Reviewer contact information is included on all design reviews for this purpose. Where discussions lead to potential changes in project scope, the Design Professional shall discuss those changes with the DASNY PM before implementing them. Prior to the bidding phase, all comments shall have been answered to the satisfaction of Design & Construction and Code Compliance units, or as may be required by other authorities having jurisdiction.

Section 4.3.12 - Cost Estimates

Cost estimates are prepared by the Design Professional and provide the basis for decisions regarding the project scope. Accurate cost estimates are paramount to a successful project. The cost estimate shall be prepared at various stages of design as specified by the Design Professional Contract for Professional Services using the DASNY [Consultant Cost Estimating Workbook](#). (See www.dasny.org/forms, select Consultant – Design drop-down menu and look for DASNY Cost Estimating Workbook)

<https://www.dasny.org/sites/default/files/inline-files/DASNY%20Cost%20Estimating%20Workbook%20corrected%20to%20be%20posted%201.23.20.xlsx>

The cost estimate format will evolve such that it will be presented in the form of the Contractor's Trade Payment Breakdown, itemized by CSI specification section and summarized by primary and secondary CSI division codes, and coordinated with the DASNY PM.

The cost estimates shall include and identify the appropriate design contingency, bidding contingency, contractor's overhead and profit, special inspection and testing costs, escalation, change order contingency and general conditions specified by the Workbook and appropriate to the scale and type of project. Upon prior written approval of DASNY, the Design Professional may prepare the cost estimate in an alternative format provided the estimate includes at a minimum, all information contained in Consultant Cost Estimating Workbook supplied format.

SECTION 4.4 - BID PHASE

Section 4.4.1 - Project Manual

The Design Professional assembles the final Project Manual (the bid set) using Front End documents located in Contract Management or PMWeb, supplemental documents prepared for the project by DASNY, supplemental documents prepared for the project by the Design Professional, the approved design documents including technical specifications and drawings, and wage rates.

Prior to sending it out for duplication, the Design Professional must submit the check set to the DASNY Construction Project Manager, Construction Contract Administrator and Cost Control Analyst for review and approval. The Contract Administrator checks that the bid set includes the current version of each DASNY boilerplate document, and if necessary, provides the current version for substitution in the bid set.

At the time of bid, the Project Manual will consist of the following documents in this order:

- Project Manual Cover sheet
- Front End Documents Cover Sheet and Table of Contents
- Construction Bidding Requirements Cover Sheet
- Notice to Bidders
- Information for Bidders
- DASNY Visitor COVID-19 Screening Questionnaire
- Form of Bid, including placeholder pages for alternates and allowances
- Minimum Qualifications Form
- DASNY Omnibus Certification
- W-9
- Form of Bid Bond
- Construction Contract Forms Cover Sheet
- Scope Verification Form
- (CCA-2) – Instructions
- (CCA-2) – Definitions
- (CCA-2) – FORM
- (CCA-2) – Attachment A
- (CCA-2) – Attachment B
- (CCA-2) – Attachment C
- Insurance Form
- Agreement – Payment Bond – Performance Bond
- Construction General Conditions Cover Sheet
- General Conditions for Construction
- Supplemental General Conditions, if any
- New York State Prevailing Wage Rates
- General Requirements
- Project Schedule or Milestone Dates
- Contractor's Submittal Schedule
- A List of Required Special Inspections
- List of Technical Specifications and Drawings
- Technical Specifications
- Drawings
- Appendices, if any

DASNY prepares and furnishes the Notice to Bidders to the Design Professional. DASNY also prepares Information for Bidders, addressing project-specific requirements such as subcontractor limits, bid security, affirmative action goals, the date, time and place of the bid opening, the time of completion and liquidated damages, any pre-award requirements, and other information relevant to the bid.

The Design Professional prepares the following:

- Cover sheet
- Table of contents
- Contractor's Schedule of Values: The form must include C.S.I. numbers, work items, and units of measure, in Microsoft Excel, in sufficient detail to compare bids and to evaluate the percentage of work complete when authorizing payments. The DASNY PM can provide a sample Schedule of Values.
- Contractor's Submittal Schedule: The Design Professional specifies the submittal items that are required to be reviewed to confirm that the design intent will be met, and the closeout items (record drawings, special warranties, etc.) required for the project. The Contractor's Submittal Schedule report is printed from DASNY's Project Management System and included in the Contract Documents.
- Modifications to the General Requirements (if any): see below
- Project schedule
- List of technical specifications and drawings: The Design Professional must identify each specification and drawing included in the Contract Documents, updating the list during design development.
- Technical specifications
- Appendices: The Design Professional may include other information for use in bidding or administering the project, such as soil borings, test reports, permits and applications, or other special instructions to contractors. Any appendices must be listed in the table of contents, dated and attributed, and preceded by a title page in the Project Manual.

Section 4.4.2 - Modifications to the General Requirements

The General Requirements address conduct of the construction project, describing work under the contract, alternates and allowances, and many project-specific topics such as access to the site, working hours, security, temporary facilities, heat during construction, storage and protection of material and equipment, project close-out, project record documents, and warranties, guarantees, and bonds. DASNY maintains versions of the General Requirements for single prime contracts and for multiple prime contracts.

The Design Professional is required to modify the General Requirements, and the technical specifications in coordination with DASNY and the Client. The DASNY PM can provide a sample document with formatting. The Design Professional, in turn, provides an electronic version of the final document, in Microsoft Word (showing all Edits), to the DASNY PM for review.

Section 4.4.3 - Alternates

Alternates are additional items or project enhancements desired by the client that are not part of the base project program. A list of add alternates, ordered by priority, is developed collectively by the client, the Design Professional and DASNY. In certain circumstances, DASNY may instruct the Design Professional to include a deduct alternate; otherwise, deduct alternates are not permitted. If bids come in under budget, the client may accept alternates that, when added to the base bids, do not exceed the authorized construction budget. To maintain the integrity of the competitive bidding process, alternates accepted by the client must be awarded in the order of priority stated in the Bid Documents.

The Design Professional is required to design a completely functional project without the inclusion of alternates, providing separate estimates for the base project and each alternate. Alternates, if any, should be fully described in the technical specifications, and/or on the drawings, as appropriate, and in the Supplemental General Requirements Section 012300 - Alternates.

DASNY's standard Form of Bid includes a placeholder page and DASNY will provide "Form of Bid Alternate" form as required. The Form of Bid is supplied with other Contract Documents to the Design Professional by the Procurement Department.

Section 4.4.4 - Allowances

Allowances are stipulated amounts that contractors are instructed to include in their base bids for items of required Work that cannot be completely described in the Contract Documents. Allowances provide a means of controlling the cost of such Work; if the entire allowance is not used, DASNY takes a credit for the unused portion.

Occasionally, allowances are used to procure proprietary products or services if pre-approved by DASNY's President. The DASNY PM is responsible for securing the required approval to specify proprietary products or services, and the Design Professional must provide sufficient information and document to secure these approvals before the 60% submission.

Allowances should be fully described in the technical specifications, and/or on the drawings, as appropriate, and in the Supplemental General Requirements Section 012100 - Allowances.

DASNY's standard Form of Bid includes a placeholder page and DASNY will provide Form of Bid Allowance form, if required, on which any allowances are itemized with the amount to be included in the contractor's base bid. The Form of Bid is supplied with other Contract Documents to the Design Professional by the Procurement Department.

Section 4.4.5 – Schedule of Allowances

The use of unit price allowances is generally not acceptable, except on projects where this method of measurement and basis of payment is suitable, such as site work or roadwork. In some situations, the establishment of unit prices for additional work at the time of bid may be appropriate. If unit prices are being considered, contact the DASNY PM and Chief, Procurement - Construction Contract's Unit, for instructions.

Section 4.4.6 - Bid Documents

The result of the design phase is the production of the Bid Documents. The Bid Documents establish the contractual obligations between DASNY and the Contractor, and upon execution of a contract between DASNY and the Contractor, become the Contract Documents.

Upon satisfactorily addressing the review comments, the DASNY PM will prepare the DASNY Pre-Bid Summary. At this time, the DASNY PM will also prepare the NYS Contract Reporter Advertisement and forward it to the Construction Contracts Unit for publication in the NYS Contract Reporter and on the DASNY web site.

The Notice to Bidders, Information for Bidders, and any special bid form requirements are inserted into the Project Manual, the documents are given a final check, and transmitted to DASNY's term printer for printing.

DASNY utilizes Electronic Bid Documents through its term printer and as such, eliminates the need for the Design Professional to distribute bid sets and manager bid set deposits and plan holder reporting. At the time of the design kickoff meeting (or when appropriate), the DASNY PM will review with the Design Profession the use of the DASNY term printer and the use of its [public planroom](#), information regarding file naming and format, transmission of final bid documents, and DASNY's term printer contact information.

The Design Professional must seal and sign the Project Manual cover sheet and all drawings, including title

sheets and electronically send the PDF (Portable Document File) format files to DASNY's term printer. Once DASNY's term printer advises that they have setup the project's planroom, the Design Professional should review the project's planroom and determine if all information is included and correct and notify the DASNY PM of their findings.

The plan holders list will be maintained by the DASNY term printer as documents are issued to contractors. The plan deposit is non-refundable, and is determined by the DASNY term printer, at market rates, prior to documents being available for pick-up.

Section 4.4.7 - Pre-Bid Meeting

The Pre-Bid Meeting is scheduled by the DASNY PM prior to the project being advertised for bid, when the Pre-Bid Summary is prepared. The date, time and location must be coordinated with the facility or institution. The timeframe for conducting the Pre-Bid is typically at least two weeks after the project has been advertised for bidding, and about two weeks prior to the bid date. This will generally allow sufficient timeframes for prospective bidders to obtain Contract Documents prior to the Pre-Bid Meeting, and for the prospective bidders to receive any addenda. If a shorter timeframe is required, this must be reviewed with the DASNY Construction Contracts Administrator and Cost Control Analyst. Additionally, the scheduling of the Pre-Bid Meeting should take into consideration and not conflict with holidays or other observances.

The Pre-Bid Meeting is conducted by the DASNY PM or designee. The Design Professional's participation is required. The purpose of the Pre-Bid Meeting is to allow the prospective bidders to visit the project site, ask questions regarding the project, and to allow DASNY and the Design Professional to present and explain any special features regarding the project, project requirements (including LEED® and related reporting and submittal requirements), or the bid process. Attendance at the Pre-Bid Meeting by prospective bidders is highly encouraged, but generally not mandatory.

The Design Professional is to be represented at the Pre-Bid Meeting by the Design Professional's representative, and appropriate designers and sub-consultants, depending upon the project size, scope, and complexity, or as directed by DASNY's DASNY PM. The Design Professional will obtain a sign-in list of Pre-Bid Meeting attendees and provide the list to the DASNY PM. Minutes of the Pre-Bid Meeting will generally not be required. The Design Professional will issue addenda as required as a result of the Pre-Bid Meeting. Contact the construction phase manager for instructions.

Section 4.4.8 - Addenda

The Design Professional is responsible for preparing and distributing all addenda. Addenda are to be reviewed and approved by the DASNY PM, the Contracts Administrator and Cost Control Analyst before they can be issued. The DASNY PM can provide a [sample Addenda](#) with the proper language and format. The Design Professional must issue addenda. Contact the DASNY PM to determine the appropriate distribution method.

Section 4.4.9 - Bids

Bids are due at the time and location specified in the Notice to Bidders. Bids are generally received on Tuesday, Wednesday or Thursday at 2 p.m. at DASNY's Albany office.

DASNY's Procurement Department will receive, open, record and issue the bid tabulation. All bid openings will be made available for viewing live via Zoom. Bid results are available on DASNY's website one day after the bid opening.

Section 4.4.10 - Post Bid Requirements

After receipt of the bids, the Design Professional will be required to perform post bid phase services, including the comparison of its estimate to the bid breakdown of the low bidder and providing bid(s) analysis and a

recommendation on award of the contract. The recommendation to award should generally be completed within three weeks of the bid date, in order to ensure that the contract is fully executed within the contract award period.

The DASNY PM or its designee, with assistance from the Design Professional, will generally review the capabilities and qualifications of the apparent low bidder. If the Design Professional has any prior experience or knowledge of the low bidder that DASNY should consider in evaluating the low bidder, the Design Professional should advise the DASNY PM. The DASNY PM or its designee may conduct a Bid Review Meeting with the contractor to assess these items. Participation by the Design Professional may be required; contact the DASNY PM.

SECTION 4.5 - CONSTRUCTION & CLOSEOUT**Section 4.5.1 - Construction Phase**

The construction phase begins with a construction kickoff meeting. This will be scheduled by the DASNY PM at or about the time the contract with the contractor is executed and approved, depending upon the project. Attendees at the construction kickoff meeting generally include the DASNY PM, DASNY Field Representative, Design Professional, Construction Manager (if applicable), Contractor(s), and appropriate facility and client agency personnel. The agenda, provided by the DASNY PM, generally includes introduction of personnel, project overview, facility rules and regulations, security, temporary facilities, DASNY forms, shop drawings and submittals, M/WBE requirements, subcontractors and suppliers, insurance, safety, Contractor's Schedule of Values, Contractor's Labor Rate Breakdowns, Payment Application Process, Change Order Process, project communications, construction schedule, and a site visit and walk-through. Contact the DASNY PM regarding additional agenda items. The Design Professional will be required to prepare and distribute minutes of the construction kickoff meeting.

During construction, the Design Professional will be required to provide construction phase services as required by the Contract. These services generally include

- Review and approval or disapproval of all shop drawings, submittals, and mock-ups
- Review and approval or disapproval of all sustainability-related submittals and documentation
- Provide interpretations of the Contract Documents
- Review of change orders
- Attend regular job progress meetings and issue meeting minutes
- Perform periodic progress inspections of the work in progress
- Prepare and issue punch lists
- Conduct final and warranty inspections to review the project for compliance with the requirements of the Contract Documents
- Assist in obtaining client/end user acceptances, beneficial use and approvals, etc.
- Assist in obtaining notices/certificates of Substantial Completion, Physical Completion, and Final Completion, as may be required
- Assist in obtaining regulatory signoff and approval, including but not limited to Certificates of Occupancy (C of O's), Temporary Certificates of Occupancy (TCOs), Letters of Completion, etc. as may be required by the authorities having jurisdiction.

During the course of construction, the Design Professional shall verify that the Contractor is maintaining an up-to-date record of construction variances from the Design Professional's drawings issued in the bid set. At the conclusion of construction, the Design Professional shall incorporate all changes to create a set of record drawings representing all construction work performed under this scope of work. Record Drawings shall be submitted to DASNY in AutoCAD. Standard industry layer conventions, such as those published by the AIA or the National CAD Standards shall be acceptable.

Section 4.5.2 - Project Close-Out

At the conclusion of the project, punch lists are prepared by the Design Professional and completed by the Contractors. At the final inspection, a DASNY Notification of Substantial Completion (NOSC) and Notification of Project Acceptance will be executed by the Institution/Facility, Design Professional, and DASNY. Upon completion by the Contractors of the outstanding items noted on the NOSC, the Contractors may submit their final applications for payment.

Concurrently, the Design Professional shall prepare the project closeout documents required by the Contract, generally consisting of the following:

- Reproducible set of record drawings
- Electronic record drawings
-

The Design Professional shall review and approve the Operations and Maintenance Manuals (O&M Manuals), warranties and guaranties as submitted by the Contractors.

The Design Professional may also be required to provide the services necessary to obtain regulatory signoff and approval a Certificate of Occupancy or a Code Compliance Certificate (CCC), TCOs, Letters of Completion, etc. as may be required by the authorities having jurisdiction.

For projects for which NYC is the authority having jurisdiction the consultant shall perform the regulatory required services and shall provide documentation required by the various NYC agencies, NYCDOB, NYCDEC, FDNY, etc., including but not limited for NYCDOB, interim and special inspections, sign-offs, letters of completions for Alt applications, sign-offs for special use/occupancy, and for FDNY letters of approval, etc.

After final applications for payment have been submitted by the contractors, the Design Professional has provided all of the services required by its Contract, and no further services are required of the Design Professional, the Design Professional may submit its final application for payment.

The Design Professional shall inspect the Project prior to the end of the one-year guarantee periods and notify the Owner in writing as to their findings.

The Design Profession shall close out the third-party's sustainability rating system and provide the certification to DASNY, for distribution to the Owner.
